ID	Task Name	Duration	Start	Finish
1	Mitchell Ln-Skinner FDR	1 day	Fri 5/30	Fri 5/30
4	Penry	1 day	Thu 6/5	Thu 6/5
5	Roloson	1 day	Fri 6/6	Fri 6/6
48	Newhouse-Pulv	5 days	Tue 6/10	Mon 6/16
6	Curve	1 day	Wed 6/11	Wed 6/11
11	Mill Condit & CR 605	1 day	Wed 6/11	Wed 6/11
39	Guardrail	3 days	Wed 6/11	Fri 6/13
7	Piatt	1 day	Thu 6/12	Thu 6/12
8	Hollenback	0.5 days	Fri 6/13	Fri 6/13
12	Interseal Condit****	1 day	Fri 6/13	Fri 6/13
9	Cheshire-PG 70-22	0.5 days	Mon 6/16	Mon 6/16
49	Newhouse Seal*****	1 day	Mon 6/16	Mon 6/16
54	Scioto Twp-Seal	2 days	Mon 6/16	Tue 6/17
10	Porter Central	2 days	Mon 6/16	Wed 6/18
50	3B's & K- Pulv & Seal	4 days	Wed 6/18	Mon 6/23
13	Condit-Pave	7 days	Wed 6/18	Fri 6/27
41	Ag Road Oil	3 days	Mon 6/23	Wed 6/25
51	Seal 3B's & K*****	1 day	Mon 6/23	Mon 6/23
16	Mill Sunbury	1 day	Wed 6/25	Wed 6/25
46	Trenton-Pulv & Seal	5 days	Wed 6/25	Tue 7/1
14	CR 605-Pave	6 days	Fri 6/27	Mon 7/7
2	Shannnah,W.Orng,	2 days	Mon 6/30	Tue 7/1
55	Thompson-Seal	2 days	Mon 6/30	Tue 7/1
56	Radnor-Seal/MP	1 day	Mon 6/30	Mon 6/30
57	Delaware-Seal	1 day	Mon 6/30	Mon 6/30
58	Marlboro-Seal	1 day	Mon 6/30	Mon 6/30
59	Troy - Seal	1 day	Mon 6/30	Mon 6/30
60	Berlin-Seal/MP	1 day	Mon 6/30	Mon 6/30
61	Harlem-Seal	1 day	Mon 6/30	Mon 6/30
44	Crack Sealing	19 days	Tue 7/1	Fri 7/25
47	Trenton Seal****	1 day	Tue 7/1	Tue 7/1
3	Lazell, Bale Kenyon,Center Vill	3 days	Wed 7/2	Fri 7/4
40	Rejuve- PaveTech(CR605)	2 days	Mon 7/7	Tue 7/8

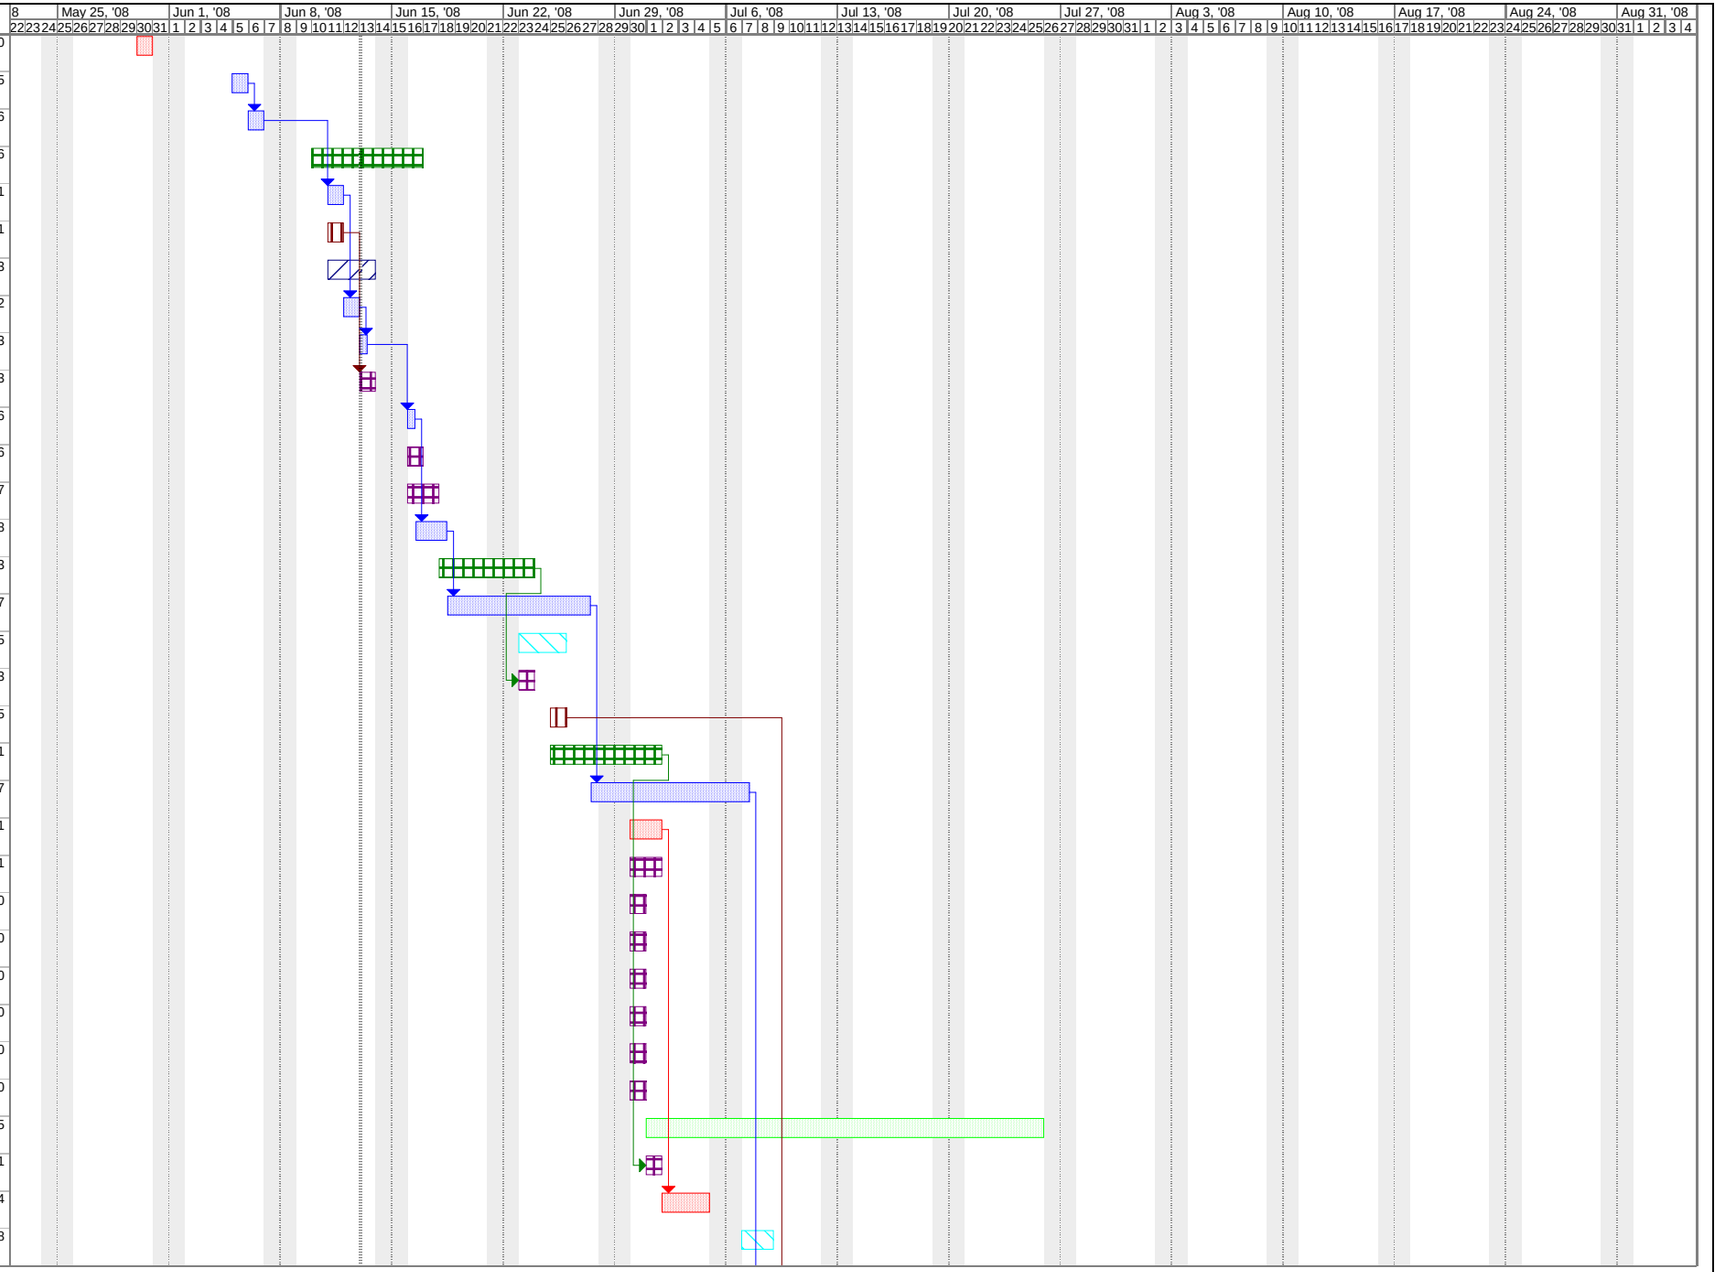
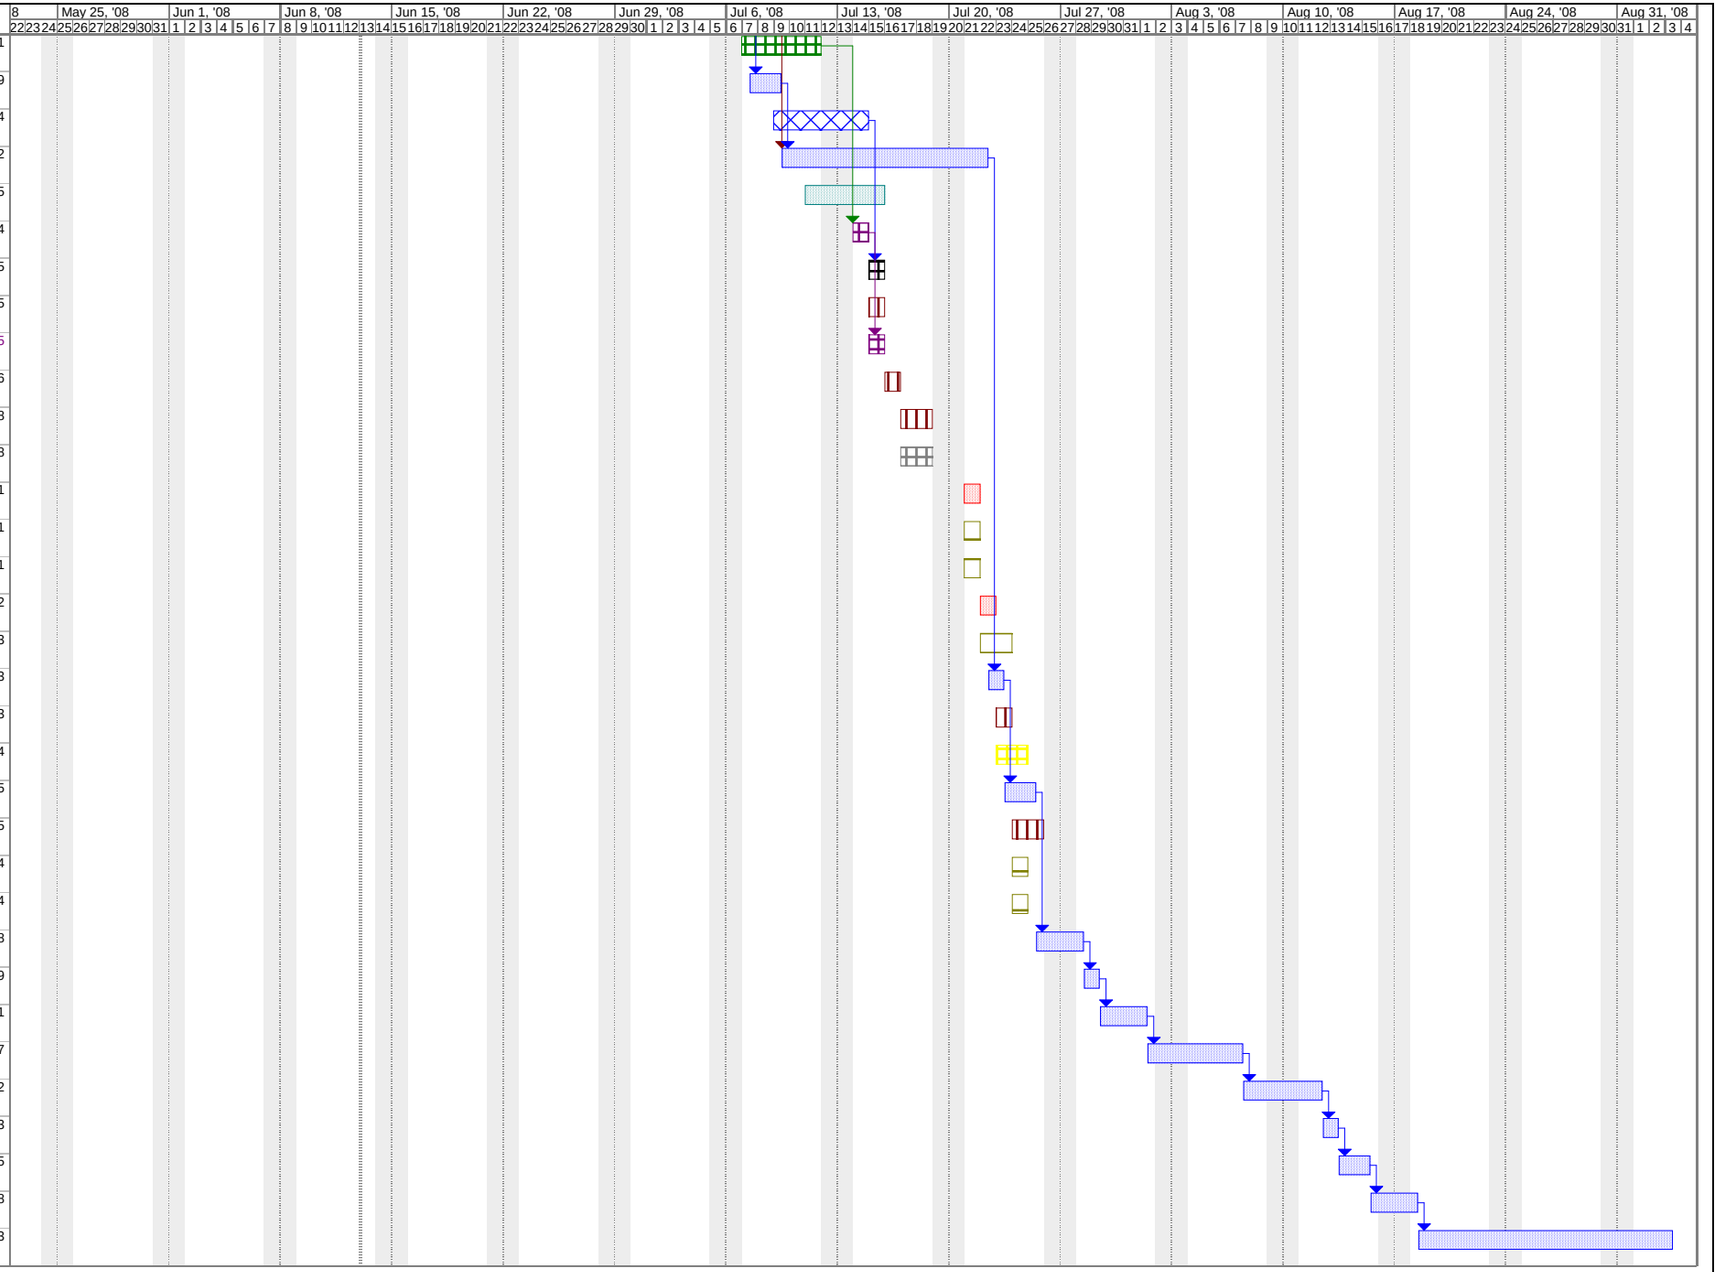
ID	Task Name	Duration	Start	Finish
52	Kelly McMaster-Pulv & Seal	5 days	Mon 7/7	Fri 7/11
15	Trenton-Pave	2 days	Mon 7/7	Wed 7/9
19	Justamere 304	4 days	Wed 7/9	Mon 7/14
17	Sunbury-Pave	9 days	Wed 7/9	Tue 7/22
45	Slurry Seal	3 days	Fri 7/11	Tue 7/15
53	Kelly McMaster Seal****	1 day	Mon 7/14	Mon 7/14
20	Justamere Prime Coat	1 day	Tue 7/15	Tue 7/15
23	Mill Big Walnut	1 day	Tue 7/15	Tue 7/15
43	Center Village Interseal***	1 day	Tue 7/15	Tue 7/15
25	Mill Genoa Group 1	1 day	Wed 7/16	Wed 7/16
27	Mill Genoa Group 2	2 days	Thu 7/17	Fri 7/18
42	Kelly McMaster Agg Drains	2 days	Thu 7/17	Fri 7/18
32	Gladshire FDR Paver 600cy	1 day	Mon 7/21	Mon 7/21
62	Greenlawn-Micro	1 day	Mon 7/21	Mon 7/21
63	Kelly McMaster-Micro	1 day	Mon 7/21	Mon 7/21
33	Fawnwood-Maple Grove-FRD	1 day	Tue 7/22	Tue 7/22
64	Condit-Micro	2 days	Tue 7/22	Wed 7/23
18	Kelly McMaster-Pave	1 day	Tue 7/22	Wed 7/23
31	Mill Waterford,Atol,Slate Run	1 day	Wed 7/23	Wed 7/23
34	Sami Orange	2 days	Wed 7/23	Thu 7/24
21	Justamere Pave	2 days	Wed 7/23	Fri 7/25
29	Mill Genoa Group 3	2 days	Thu 7/24	Fri 7/25
65	Center Village-Micro	1 day	Thu 7/24	Thu 7/24
66	Adams-Micro	1 day	Thu 7/24	Thu 7/24
22	Center Village-Pave	1 day	Fri 7/25	Mon 7/28
24	Big Walnut-Pave	1 day	Mon 7/28	Tue 7/29
26	Pave Genoa Group 1	3 days	Tue 7/29	Fri 8/1
28	Pave Genoa Group 2	4 days	Fri 8/1	Thu 8/7
30	Pave Genoa Group 3	3 days	Thu 8/7	Tue 8/12
35	Maple Grove/Fawnwood-Pave	1 day	Tue 8/12	Wed 8/13
36	Waterford-Atol-Gladshire-Pave	2 days	Wed 8/13	Fri 8/15
37	Slate Run	1 day	Fri 8/15	Mon 8/18
38	Sawmill Parkway	12 days	Mon 8/18	Wed 9/3
